

INDIANAPOLIS

DEPARTMENT OF PUBLIC WORKS

★

White River Innovation District – December Construction Update


Henry Street Bridge:

- Continued removing formwork from between bridge beams.
- All Stantec trailers and equipment were removed from the site.
- Continued setting forms and pouring sections of concrete barrier rail.
- AES began installing duct work east of the White River.
- Continued erecting ring forms at Pier #5.
- Continued driving sheet piles for wall to protect the trail from eroding, upstream of

Right: The ring on Pier 5 is taking shape.

Lower left: AES ducts on the east side of the river.

Lower right: View from under the bridge.

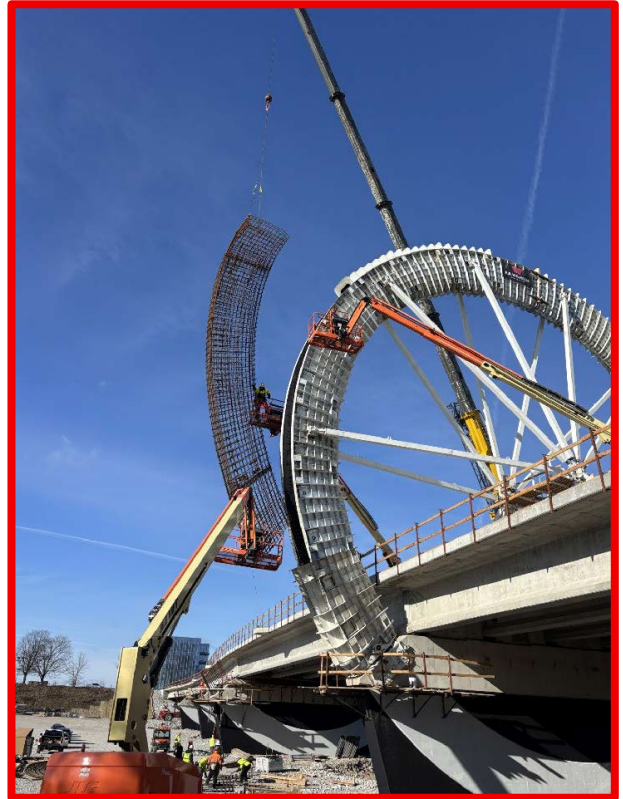

INDIANAPOLIS

DEPARTMENT OF PUBLIC WORKS

★

West Side:

- Installed pedestrian poles and push bottoms at the intersection of Oliver with White River Parkway.
- Finished placing planting soil and trees west of Division Street.
- Drove sheet piles along the west side of the White River to protect the White River Greenway Trail.
- Concrete work east of South White River Parkway is on hold due to cold temperatures.



Top: Grass and trees have been planted west of Division Street.

Bottom: View of the bridge from the west bank of the White River.



Note: For weekly, more detailed construction updates, visit indy.gov: White River Innovation District.
